



CENTERVILLE ROAD IMPROVEMENT PROJECT

DATE: August 28, 2018

SUBJECT: Centerville Road Construction Update #5
City Project No. 18-16
SAP 174-020-022 & SAP 062-659-018

Crews have completed the roadway widening work and subsurface utility construction on the east side of Centerville Road (Stage 2, see sequencing map). Crews have shifted traffic and are working to complete the new median installation work from Meadowlands Drive to the Cub Foods/White Bear Heights Apartments/Lunds/Byerly's site driveways (Stage 3). Traffic signal poles and mast arms will also be installed during this stage.

Stage 3 work is anticipated to last 3-4 weeks, with a completion date anticipated on or around September 14. Following Stage 3 work, crews will be performing a mill and overlay of Centerville Road from Highway 96 north to the CP Railroad tracks. Milling and overlay work will occur during the daytime, with temporary lane restrictions. Milling and overlay work is anticipated to take approximately one (1) week to complete.

The project is scheduled to be completed by the end of September, 2018. Periodic updates will be posted to the project website throughout the construction process.

Contacts for Construction:

Project Inspector

Rae Tressler
Alliant Engineering
612-237-9451
rtressler@alliant-inc.com

Construction Manager

Brian Connolly
Alliant Engineering
612-767-9332
bconnolly@alliant-inc.com

Contractor Foreman

Tim Matteson
Forest Lake Contracting
651-248-4708
tim@forestlakecontracting.com





City of White Bear Lake




Jesse Farrell
Assistant City Engineer
651-429-8531
jfarrell@whitebearlake.org

Attachments:

- Page 2 – Staging Map
- Page 3 – Construction Photos

Anticipated Project Staging

LEGEND	
	WORK ZONE
	TEMPORARY TRAFFIC FLOW
	EXISTING TRAFFIC FLOW
	COMPLETED IN PREVIOUS STAGE

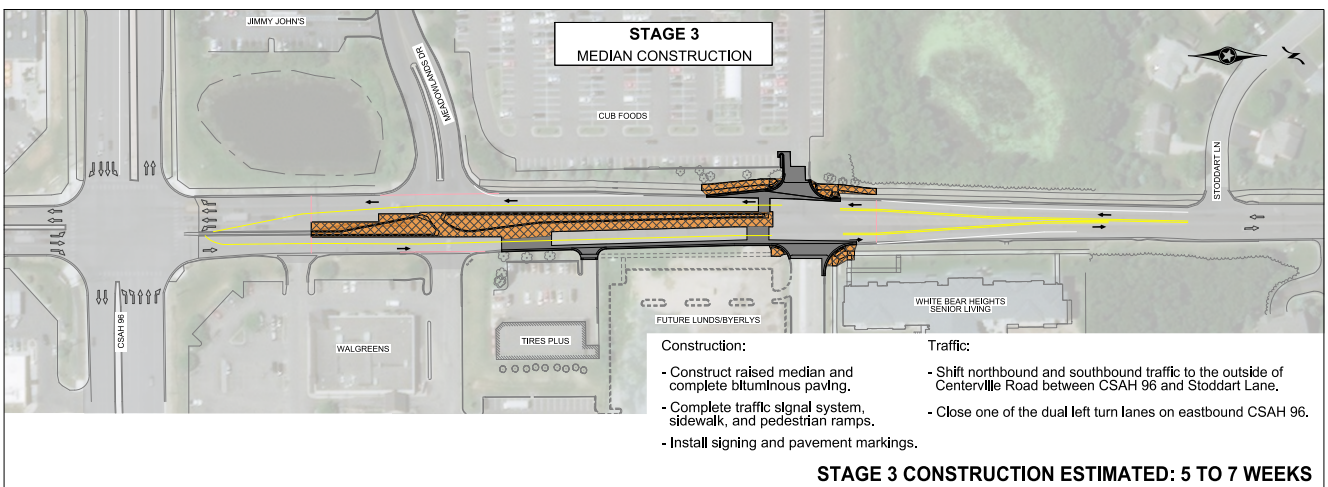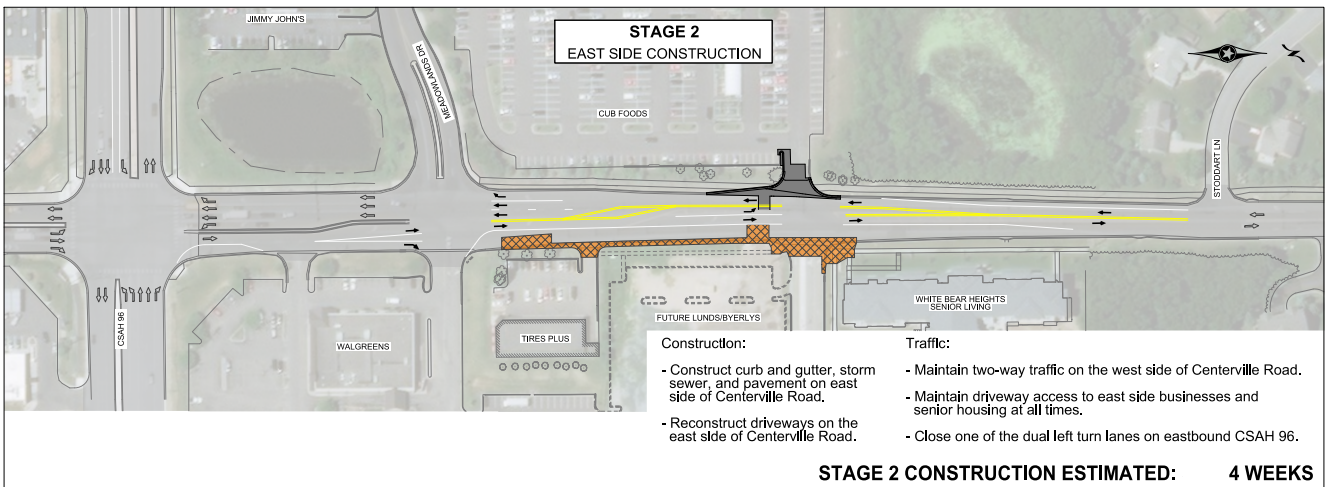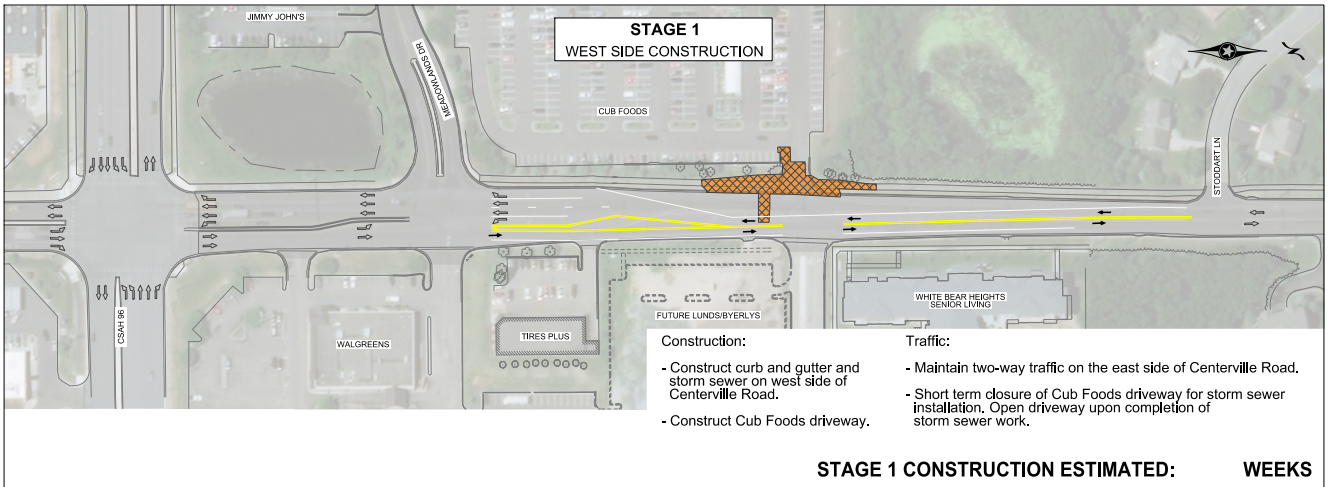

Construction Photos



Subcut – East Side (Centerville Road)



Lane Widening – East Side (Centerville Road)



Storm Sewer Installation – Median (Centerville Road)



Driveway Installation – Cub Foods
